


| ID |  | Task Mode | Task Name                                                   | Duration         | Start               | Finish              | Predecessors    | Successors | 2025  |       |       |       | 2026  |       |       |       | 2027  |       |       |       | 2028  |       |       |       | 2029  |       |       |       | 2030  |
|----|--|-----------|-------------------------------------------------------------|------------------|---------------------|---------------------|-----------------|------------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|
|    |  |           |                                                             |                  |                     |                     |                 |            | Qtr 1 | Qtr 2 | Qtr 3 | Qtr 4 | Qtr 1 | Qtr 2 | Qtr 3 | Qtr 4 | Qtr 1 | Qtr 2 | Qtr 3 | Qtr 4 | Qtr 1 | Qtr 2 | Qtr 3 | Qtr 4 | Qtr 1 | Qtr 2 | Qtr 3 | Qtr 4 | Qtr 1 |
| 1  |  |           | <b>Winchester Avenue on site</b>                            | <b>1020 days</b> | <b>Mon 06/01/25</b> | <b>Wed 07/02/29</b> |                 |            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 2  |  |           | Design and legal approval                                   | 18 mons          | Mon 06/01/25        | Wed 03/06/26        |                 | 10         |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 3  |  |           | <b>Construction</b>                                         | <b>460 days</b>  | <b>Mon 03/03/25</b> | <b>Thu 17/12/26</b> |                 | <b>10</b>  |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 4  |  |           | Construction Phase 1A                                       | 7 mons           | Tue 05/08/25        | Fri 20/02/26        |                 | 10,9       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 5  |  |           | Construction Phase 1C (s38 spine from 1B to Harestock Lane) | 175 days         | Mon 03/03/25        | Mon 03/11/25        |                 | 10,9       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 6  |  |           | Construction Phase 1B                                       | 136 days         | Wed 01/10/25        | Fri 15/05/26        |                 | 10,9       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 7  |  |           | Construction Phase 2A                                       | 40 days          | Wed 01/04/26        | Mon 01/06/26        |                 | 10,9       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 8  |  |           | Construction Phase 2B (surface course all areas)            | 165 days         | Mon 03/11/25        | Wed 29/07/26        |                 | 10,9       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 9  |  |           | RSA3 and Defect correction                                  | 5 mons           | Thu 30/07/26        | Thu 17/12/26        | 5,6,7,8,4       | 10,16      |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 10 |  |           | Monitoring period (Road open)                               | 12 mons          | Fri 18/12/26        | Mon 29/11/27        | 3,2,6,7,8,5,9,4 | 11         |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 11 |  |           | Review and assess monitoring period results                 | 6 wks            | Tue 30/11/27        | Fri 11/02/28        | 10              | 12         |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 12 |  |           | Maintenance period                                          | 12 mons          | Mon 14/02/28        | Wed 24/01/29        | 11              | 13         |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 13 |  |           | Review and assess, rectify any defects                      | 10 days          | Thu 25/01/29        | Wed 07/02/29        | 12              |            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 14 |  |           | <b>Harestock Lane Jn Andover Road</b>                       | <b>1264 days</b> | <b>Fri 17/11/23</b> | <b>Wed 22/11/28</b> |                 |            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 15 |  |           | Design and legal approval                                   | 32 mons          | Fri 17/11/23        | Mon 11/05/26        |                 | 16         |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 16 |  |           | Construction                                                | 9 mons           | Mon 11/01/27        | Thu 23/09/27        | 9,15            | 17         |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 17 |  |           | RSA3 and Defect correction                                  | 35 days          | Fri 24/09/27        | Thu 11/11/27        | 16              | 18,21      |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 18 |  |           | Maintenance period                                          | 12 mons          | Fri 12/11/27        | Wed 22/11/28        | 17              |            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 19 |  |           | <b>Stoney Lane Jn Andover Road</b>                          | <b>1370 days</b> | <b>Fri 16/02/24</b> | <b>Mon 30/07/29</b> |                 |            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 20 |  |           | Design and legal approval                                   | 32 mons          | Fri 16/02/24        | Tue 11/08/26        |                 | 21         |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 21 |  |           | Construction                                                | 7 mons           | Fri 12/11/27        | Wed 28/06/28        | 20,17           | 22         |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 22 |  |           | RSA3 and Defect correction                                  | 35 days          | Thu 29/06/28        | Wed 16/08/28        | 21              | 26,23      |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 23 |  |           | Maintenance period                                          | 12 mons          | Thu 17/08/28        | Mon 30/07/29        | 22              |            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 24 |  |           | <b>Andover Road 'middle section'</b>                        | <b>1449 days</b> | <b>Tue 28/05/24</b> | <b>Fri 01/03/30</b> |                 |            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 25 |  |           | Design and legal approval                                   | 32 mons          | Tue 28/05/24        | Fri 20/11/26        |                 | 26         |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 26 |  |           | Construction                                                | 6 mons           | Thu 17/08/28        | Wed 31/01/29        | 25,22           | 27         |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 27 |  |           | RSA3 and Defect correction                                  | 35 days          | Thu 01/02/29        | Wed 21/03/29        | 26              | 28         |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 28 |  |           | Maintenance period                                          | 12 mons          | Thu 22/03/29        | Fri 01/03/30        | 27              |            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |

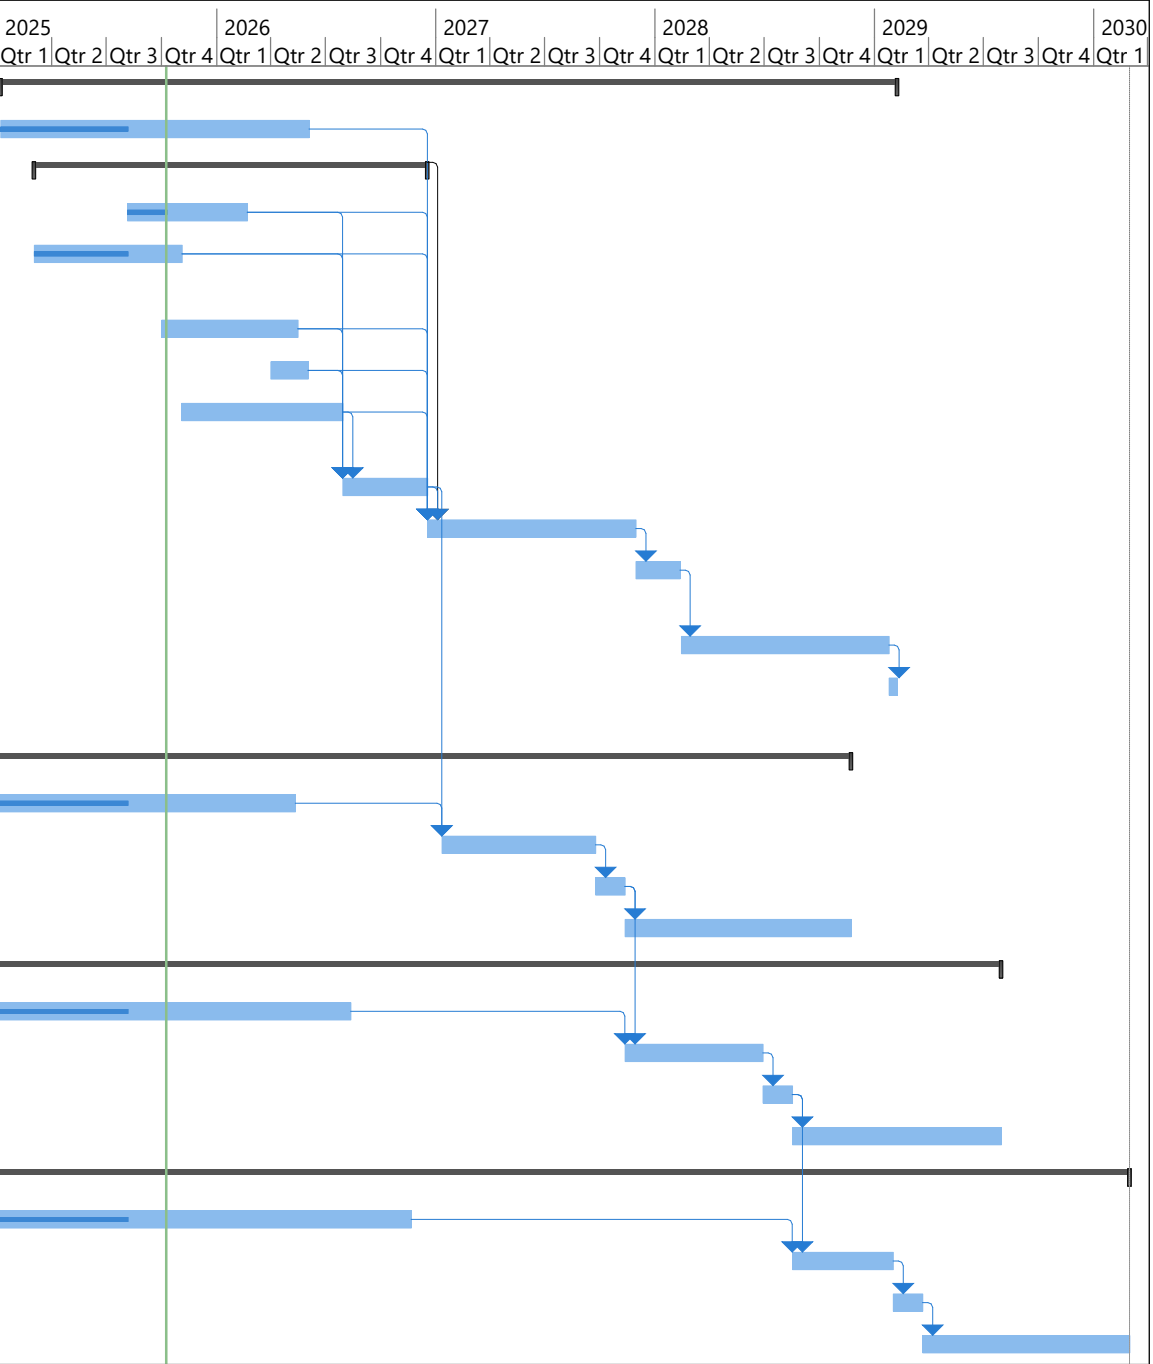

Project: Kings Barton simple pro  
Date: Thu 09/10/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

Page 1
