KINGS BARTON SECTION 106 LEGAL AGREEMENT - KEY OBLIGATION TRACKER May 2025*

Winchester City Council Legal Agreement dated 8/3/11 (link below)

Hampshire County Council Legal Agreement 7/3/11 and variations of 11/10/13, 24/5/22. Text of the latest Deed of Variation (June 2025) agreed and being signed and key changes are included below.

Please note that this table includes the key planning obligations set out within the s106 legal agreements for Kings Barton only. The development is also subject to a number of planning conditions which are attached to the planning permission decision notices for the site.

These permissions are available on the WCC website

Council Tax records on 2/6/25 indicate 688 units registered on the site (including 2 unoccupied)

S106 Para	Summary of Requirement	Oblig ation with WCC or HCC?	Category	When is it required?	What is the latest status?	Further Information
2.4	Phasing Programme - to show the order in which the developer will construct the phases.	wcc	General	Prior to commencement	Completed	
3.7	Draft Affordable Housing Masterplan Strategy - to demonstrate the location and total number of affordable units across the development	WCC	Affordabl e Housing	Prior to commencement	Completed	
3.8	Draft Affordable Housing Reserved Matters Strategy - to demonstrate how individual applications will take account of the overall	WCC	Affordabl e Housing	Prior to commencement	Completed	

	Masterplan Strategy (in terms of layout and					
	number)					
	Local Lettings Plan - to show how certain					
	properties are allocated to certain groups of					
	people in order to create and maintain a		Affordabl	Prior to		
3.21	sustainable community.	WCC	e Housing	commencement	Completed	
						Agreed via the Landscape
						Open Space Specification
						document, which specifically
	Long Term Ownership, Maintenance and			Prior to		references Condition 16 and
	Management Plan - to includes details of Open		Landscap	occupation of a		also Clauses 4 and 5 of the
5.1	Spaces and any other landscaped land.	WCC	е	relevant phase	Completed	S106.
			Culture			
			and	Prior to		
	Cultural Facilities Contribution - to provide		Communi	occupation of the		800 units not constructed to
6.1	£50,000 for cultural facilities	WCC	ty	800th unit	Upcoming	date
			Culture			
	Specification of the Community Centre - to		and			Copy of specification provided.
	ensure the Community Centre includes		Communi	Prior to		Submitted May 2014 in
7.1	adequate facilities and internal spaces.	WCC	ty	commencement	Completed	accordance with Clause 7.1
			Culture			
	Complete the Community Centre - in a good and		and	Prior to the		
	workmanlike manner and using good quality		Communi	occupation of the		800 units not constructed to
7.6.2	materials	WCC	ty	800th unit	Upcoming	date
			Culture			
			and	Prior to the		
			Communi	occupation of the		800 units not constructed to
7.8	Transfer the Community Centre to the Council	WCC	ty	800th unit	Upcoming	date.

8	Community Development Worker - to provide a Worker (which may be an employee of the Council)	WCC	Culture and Communi ty	Prior to the occupation of the 200th unit	Completed	Implementation Officers and dedicated Senior Planning Officers for the role employed by the Council
8	Community Development Worker Accommodation - provide a space for use by the Community Development Worker	WCC	Culture and Communi ty	Prior to the occupation of the 200th unit	Completed	Worker employed by Council with access to on-site facilities at Visitor Centre if required.
g	Public Access Routes - to show routes across the site which the public can use at all times	WCC	Transport	Prior to commencement	Completed	
	Plan showing a detailed route from Andover					To submit to WCC for approval (1) a detailed route for the public footpaths from Andover Road through the site and the ecology amenity land to Worthy Road; (2) surfacing and other construction details for public footpaths and (3) proposals for the long term
10	Road to Barton Meadows - to include surfacing and construction details and long-term maintenance	wcc	Transport	Prior to	Completed	maintenance and management of the amenity land.

						Management and Maintenance Plan (JSL1980_873M, 11 November 2016) approved in 2016. This included 10-year programme for habitat establishment and that WCC or a third party
						would take over the management on a 125 year
					Proposals	lease from CALA.
	Developer to agree proposals for the long term				agreed and	Land transfer from owner to
	management and maintenance of 'Ecological Amenity Land' (Barton Meadows/ LEORL) with		Landscap	Prior to	subsequent land transfer	HIWWT agreed and contract largely drafted.
10.1	wcc.	WCC	e	Commencement	in progress.	<u> </u>
	Notice of Commencement 10 days before			Prior to		
4.1	construction	HCC	General	commencement	Completed	
4.5.1	Copies of all surveys - to be provided to the County Council	HCC	General	Prior to commencement	Completed	
4.5.1	County Council	1100	General	Within 3 months	completed	
				of		
				commencement,		
				prior to		
4.5.2	Design for the infrastructure serving the Primary School Land	HCC	Education	occupation of 1st unit	Completed	
4.5.2	SCHOOL LAND	псс	Euucation	Within 3 months	Completed	
				of		
				commencement,		
				prior to		
4.0	Romaya Canstraints from Drimary School Land	ПСС	Education	occupation of 1st	Completed	
4.6	Remove Constraints from Primary School Land	HCC	Education	unit	Completed	

4.7	Draft Primary School Land Transfer Plan Transfer Freehold of Primary School Lane and	НСС	Education	Within 3 months of commencement. Prior to the occupation of the	Completed	
4.8	pay first Primary Education Contribution Provide Services and Utilities to the Primary School Land	HCC HCC	Education Education	Prior to the occupation of the 150th Unit	Completed Completed	
4.10	Construct Permanent School Access and pay second Education Contribution	НСС	Transport	Prior to the occupation of the 250th unit	Part completed. Education payment has been made. Trigger for permanent access provision varied on 24/5/22.	Trigger varied 24/5/22 to read 'Not to Occupy any part of the Development within the areas shaded pink and marked 'Phase 2b' on the phasing plan unless and until the Permanent access to the primary school land has been constructed and completed to the satisfaction of HCC.'
4.11	Owner to recalculate Primary Pupil Product If the Primary Pupil Product (4.11) exceeds 420, the developer cannot occupy more than 100 further units until an additional contributon has been paid to the County Council	HCC HCC	Education	Following occupation of the 1200th unit Following occupation of the 1200th unit	Upcoming	1200 units not constructed to date 1200 units not constructed to date

4.15	Secondary Education Contribution (£3,000,000 index linked) to be paid to HCC Owner to calculate the Secondary Pupil Product	нсс	Education	Prior to the occupation of the 750th unit Following occupation of the 1200th unit	Upcoming Upcoming	750 units not constructed to date 1200 units not constructed to date
4.17	Highway Access Contribution Payments	нсс	Education	Prior to occupation	Completed	
4.18	Second Highway Access Contribution Payments	НСС	Transport	Prior to Occupation of the 650th unit	Completed	To pay Second City Access Contribution, the Second Eastern Access Contribution, the Second Western Access Contribution and the Second Non Motorised User Contribution to HCC (triggers varied in deed dated 24/5/22). HCC has confirmed second payments received in April 2025.
4.20 A (s106 variatio n 22.05.22)	To pay the Andover Road/Bereweeke Road Improvement Contribution To provide first Bus Subsidy	нсс	Transport	Within 14 days of signing the agreement Prior to the occupation of the 350th units	Completed	To pay £331,748 index linked to enable HCC to deliver the works shown indicatively on drawing 0710-64/Figure 4.9 which is pasted below (see full definition below from HCC s106 Deed of Variation 24/5/22)

4.2	4 To provide Bus Subsidy payment	HCC	Transport	Prior to the occupation of the 650th unit	Completed	HCC has confirmed second payments received in April 2025.
4.2		НСС	Transport	Prior to the occupation of the 950th unit	Upcoming	950 units not constructed to date
4.2	6 To provide Bus Subsidy payment	НСС	Transport	Prior to the occupation of the 1250th unit	Upcoming	1250th units not constructed to date
4.	To pay the Travel Plan Fee	НСС	Transport	Prior to the first occupation	Completed	
4.	Submission of school and residential Travel Plans	нсс	Transport	Prior to commencement of each phase	Part- Completed	Completed on a phase-by- phase basis and will continue to be submitted as the development is constructed. Residential Travel Plan has been approved and has been implemented. School and retail will be completed by other developers.
4.	25 To pay the Travel Plan Monitoring Fee	НСС	Transport	Prior to commencement	Completed	
4.20	5.1 Submission of Retail Travel Plan	НСС	Transport	Prior to occupation of retail units	Completed	
4.20	Not to occupy any residential unit until the Residential Travel Plan is submitted	НСС	Transport	Prior to occupation of 1st unit Prior to	Completed	
4.	To pay Travel Plan bond	НСС	Transport	commencement	Completed	

ı			İ	Ī	1		1
					Prior to the		
					occupation of the		
	4.32	Community Travel Website	HCC	Transport	350th unit	Completed	
					Prior to the		
					occupation of the		
	4.33	Installation of Travel Boards	HCC	Transport	350th unit	Completed	
ŀ	7.33	installation of Travel Boards	TICC	Transport	330th dillt	Completed	
					_		
					Prior to the		
					occupation of the		
Į	4.35.1	Pool Car Club Provision	HCC	Transport	400th unit	Completed	
		Davian the same lub ashome and previde second			Review at 700th		
	4.35.2	Review the car club scheme and provide second	LICC	Transport		Uncoming	
ŀ	4.35.2	car at 750th occupation	HCC	Transport	occupation Prior to	Upcoming	
	4.36	Sahama far Cuala Barking	HCC	Transport		Completed	
-	4.30	Scheme for Cycle Parking	псс	Transport	commencement	Completed	Fach weit mount be arreaded
							Each unit must be provided
							with cycle parking prior to
							occupation - this is an on-going
					Prior to		requirement through lifetime of development to be applied
						Dort	to each unit before it is
	4.37	Construct Cycle Barking	нсс	Transport	occupation of any	Part-	
ŀ	4.5/	Construct Cycle Parking	псс	Transport	housing unit	Completed Part-	occupied.
					Prior to the		
					Occupation of	Completed. Route open,	
					more than seven	however	
		Construct the Link Road Works to binder course			hundred and fifty		
		level and shall make the Link Road			· · · · · · · · · · · · · · · · · · ·	ongoing diversions in	Clause inserted by \$106 deed
	4 274		1100	Transman	(750) Housing		Clause inserted by s106 deed
	4.37A	Works open for use by traffic/pedestrians.	HCC	Transport	Units	place while	of variation June 2025

					road	
					completed.	
					·	
	Submit Draft Construction Route Management			Prior to		
4.38	Plan	HCC	Transport	commencement	Completed	
				Prior to		
	Approval of Draft Construction Route			occupation of 1st		
4.39	Management Plan	HCC	Transport	unit	Completed	
SCHEDU						
LE 2 Part	Submission of Access details for Andover			Prior to		
1	Road/Temporary Access Junction	HCC	Transport	commencement	Completed	
SCHEDU						
LE 2				Prior to		
PART 2	Completion of Highway Access Works	HCC	Transport	commencement	Completed	
						Schedule 2, Part 5 of
						agreement (which included
	Submission and written approval of					triggers for various stages of
SCHEDU	Implementation Programme (of various			Prior to		highways works) deleted by
LE 2	highway works see full definition below*) to the			occupation of 725		deed of variation June 2025
PART 5	County Council.	HCC	Transport	Housing Units	Upcoming	and replaced by this clause.
SCHEDU	Completed Well House Lane Rail Arch			Prior to		
LE 2	Improvement Works and Barton Farm/Worthy			occupation of		
PART 6	Road Improvements	HCC	Transport	425th unit	Completed	

SCHEUL E 2 PART 7	New Andover Road Works, Andover Road/Harestock Road Junction Improvement Works, Andover Road/Stoney Lane Junction Improvement Scheme and Andover Road/Well House Lane Junction Improvement Works	нсс	Transport	Prior to occupation of 1000th unit	Not yet triggered	Trigger pushed back from 750 to 1000 units by deed of variation of June 2025
SCHEDU LE 2 PART 8	Completion of the Downgrading of Andover Road Works to the satisfaction of the County Council and to Completion Certificate Standard	нсс	Transport	Prior to occupation of 1050th occupation	Not yet triggered	Trigger pushed back to 1050 units by deed of variation of June 2025
SCHEDU LE 2 PART 14	Where a TRO is obtained prohibiting the use of that part of Andover Road, the owner shall get county approval of landscaping with a programme for implementation and subject to the grant of all necessary licences and carry out to the approval of the County Council	нсс	Transport	Prior to occupation of 950th unit	Upcoming	Where a stopping up order or road traffic regulation order is obtained prohibiting the use of that part of Andover Road before the date of Occupation of nine hundred and fifty (950) Housing Units the Owner shall submit to the County Council for their approval details of landscaping thereof together with a programme for implementation and subject to the grant of all necessary licences by the County Council as highway authority shall carry out such landscaping to the reasonable satisfaction of the County Council in accordance with the approved

			details. 950 units not constructed to date

NOTE

KEY DEFINITIONS AND PLANS

* Definition of 'Implementation Programme' set of in deed of variation June 2025;

"Implementation Programme" means a programme to be submitted and approved by the County Council in accordance with Paragraph 5 of Schedule 2, which will set out the detail of how and when all actions/agreements/traffic regulation orders/works etc will need to be delivered in order for Andover Road to be closed to through traffic and for highway rights to be established and all traffic to have been re-routed to Winchester Avenue which for the avoidance of doubt relates to the New Andover Road Works, the Andover Road/Harestock Road Junction Improvement Works, the Andover Road/Stoney Lane Junction Improvement Works and the Andover Road/Well House Lane Junction Improvement Works and to include a programme for delivering the Downgrading of Andover Road Works.


"Link Road Works" means the section of proposed highway works that will link Phase 1B to Phase 2A including pedestrian and cycle facilities as shown indicatively on the Link Road Works Plan

"Link Road Works Plan" means the indicative plan showing the proposed link road connecting Phase 1B and Phase 2A or such other plan to be agreed in writing with the County Council at Appendix 1 of this Deed.'

"New Andover Road Works"


"Permanent Access"

means the permanent vehicular and pedestrian access complete with binder course level surfaced footways signing lining landscaping lighting and kerbing constructed pursuant to a Highway Agreement or otherwise to adoptable standards and which is connected to an adopted highway to serve the Primary School;

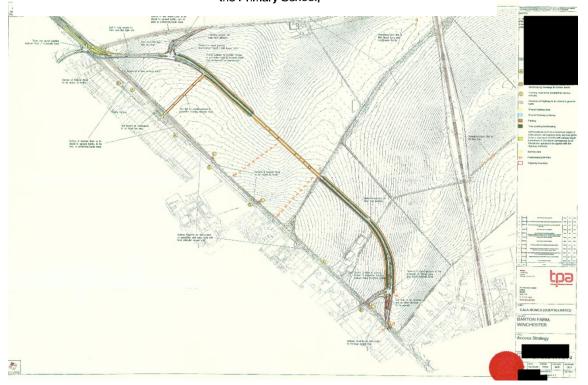

means the realignment of Andover Road through the Site with a 30mph speed limit (20mph through the local centre) as shown indicatively on drawing number 0710-64/ Figure 4.1 Rev L (as appended to this Agreement) and in accordance with the initial Design Code and the Design code Addendum Letter exchanged between the County Council and the Owner as set out in correspondence in Appendix SCG/A of the Highways Statement of Common Ground;

"Andover Road/ Bereweeke Road Junction Improvements Contribution" means the sum of Three Hundred and Thirty One Thousand Seven Hundred and Eighteen pounds (£331,718) to be paid to enable the County Council to deliver the works shown indicatively on drawing number 0710-64/Figure 4,9 annexed hereto or any other such works to deliver an amended or alternative junction improvement scheme for Andover Road which may include improvements to sustainable travel

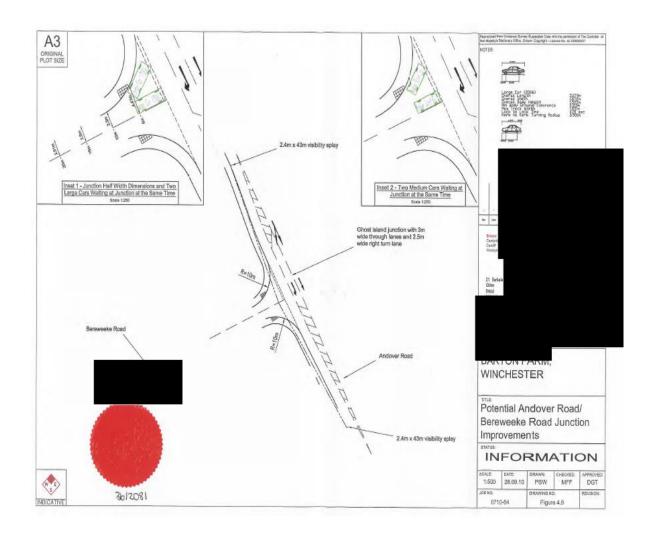

Extract from Deed of Variation 24/5/22

The definition of "Downgrading of Andover Road Works" in clause 1.1 (Definitions) of the Original Agreement shall be deleted and replaced with the following new definition:

Downgrading of Andover means the downgrading of Andover Road to a pedestrian/cycle route with vehicular access for local frontages only (subject to the provisions of Schedule 2)

Phasing Plan attached to Deed of Variation dated 24/5/22

