Public Document Pack Winchester City Council

Meeting North Whiteley Development Forum

Date and Time Monday, 17th July, 2023 at 6.00 pm.

Venue Virtual via Microsoft Teams and streamed live on YouTube at

www.youtube.com/winchestercc

SUPPLEMENTARY AGENDA

The following document was not available at the time the agenda was published and so has been published separately here.

Agenda Item.

8. Developer and Implementation Officer - A verbal update (Pages 3 - 18)

()


City Offices Colebrook Street Winchester SO23 9LJ Laura Taylor Chief Executive

All of the Council's publicly available agendas, reports and minutes are available to view and download from the Council's <u>Website</u> and are also open to inspection at the offices of the council. As part of our drive to minimise our use of paper we do not provide paper copies of the full agenda pack at meetings. We do however, provide a number of copies of the agenda front sheet at the meeting which contains the QR Code opposite. Scanning this code enables members of the public to easily access all of the meeting papers on their own electronic device. Please hold your device's camera or QR code App over the QR Code so that it's clearly visible within your screen and you will be redirected to the agenda pack.



27 July 2023

Agenda Contact: Matthew Watson, Democratic Services Officer mwatson@winchester.gov.uk 01962 848 317











North Whiteley Development

BRIEFING NOTE

North Whiteley Forum

Meeting 17th July 2023





Station Hil **Botley Road** Junction Northern Access Western Access Junction (WAJ) Curbridge Extension of Whiteley Way Extension of Bluebell Way Farm Roundabout Whiteley Town Centre Marjoram Way Parkway North Parkway South M27 Junction 9 A27 Proposed Highway Improvements Secondary School Primary School

North Whiteley Overview Plan November 2020 North Whiteley Consortium

Stanted

Overview - Highways

- Development Highways & Whiteley Way R3 to R2 delivered by the North Whiteley Consortium
- M27 / R1 Parkway South update by Hampshire CC

North Whiteley Development – North Whiteley Forum

BRIEFING NOTE - Meeting 17 July 2023



Phase 1 Bluebell Way

- Highway Opened to the Public 12th Feb 2021.
- Bus Service due commenced 9th Jan 2023
- Contract for the development of the Southern Local Centre close to agreement

North Whiteley
Package 1 - Bluebell Way
November 2020
North Whiteley Consortium

Primary School








Phase 1 Bluebell Way: (June 2023)



Phase 1 Bluebell Way Central (Jun 2023)

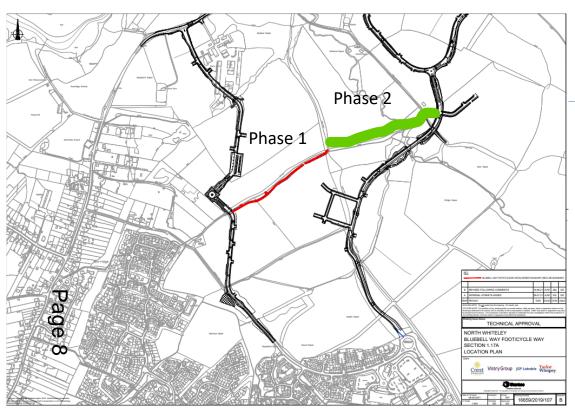

Strategic Cycleway: Footpath 9

- Phase 1 Planning Permission granted
- Technical Approval granted
- Planning application does not affect Phase 1
- Phase 1 S278 Legal Agreement agreed in principle but not yet in place
- Phase 1 Footpath Diversion application lodged
- Phase 1 Construction: Planned Summer 2023
- Phase 2 Design underway –Planning application
 Summer 2023





0 Sawpit Watercl (R3) Whiteley .opse Farm Roundabout Copse Whiteley Town Centre Page Marjoram Way Whiteley (R1a) Parkway North Proposed Highway Improvements

Phase 2 - Off Site Whiteley Way

- s278 legal agreements completed June 2022
- Works let January 2023.
- Permit to Work processes almost complete
- Utility Diversion delay at Culvert R2-R1a
- Likely start in January 2024
- Target Works Completion: Late Summer 2025

North Whiteley
Package 3 - NWC Whiteley Way
November 2020
North Whiteley Consortium





Shawfords Lake Station Hill Junction **Botley Road** Grange Farm Northern Access Junction (NAJ) Westerb Access Juncan (WAJ) Curbridge Way Extension of Whiteley Way (R3) Whiteley Extension of Farm Roundabout Botley Wood Bluebell Way Primary School

Stantec

Phase 3 - Station Hill - Whiteley Way / **Curbridge Way to Whiteley Way**

- Northern Access Junction to Whiteley via Curbridge Way complete.
- Safety Audit Curbridge Way 14 July 2023.
- Whiteley Way (East): Completion of Finishes in early August.
- Opening subject to Safety Audit Report and to Consortium decision to open Curbridge Way in isolation.
- Note that these roads will run through Development areas under construction.







Whiteley Way (East) (June 2023)



Phase 3 Whiteley/Curbridge Way - June 2023



Phase 3 Curbridge Way (July 2023)



Phase 3 Whiteley Way South (Jan 2023)

Housing Delivery (@ 17th July 2023)


Detailed Planning Permission granted for 3,065 Houses (85% of total)

1,735 Houses started

Of which 1,096 Houses Construction Mortgage Lending CML ready

Of which **1,040 Houses occupied**




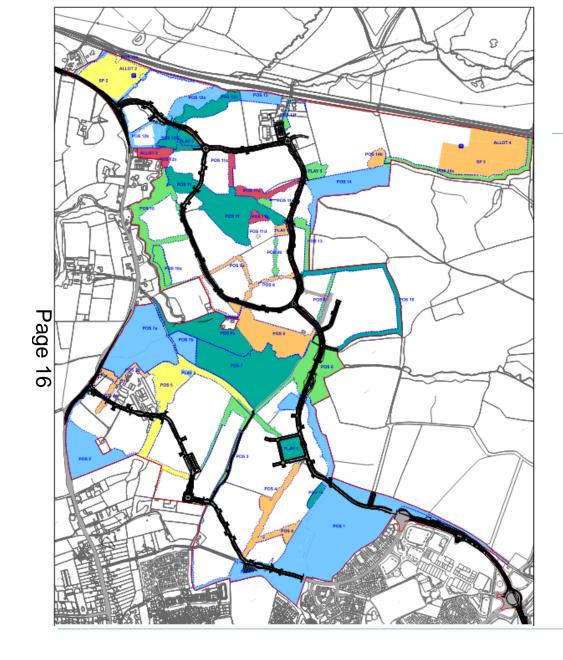

Open Space – Delivery Update

- Allotment 1 complete
- LEAP 2 (POS 5) & LEAP 3 (POS 12) completed
- LEAP 1 will be complete Autumn 2023
- Land Transfer Processes underway.
- Landscape works planned for Autumn/winter 2023
 - Area Group 1 POS 1, 2, 7A, 7B
 - Area Group 2 POS 1A, 7, 8A, 15
 - Highways (BB Way & Whiteley Way South)

Bus Service

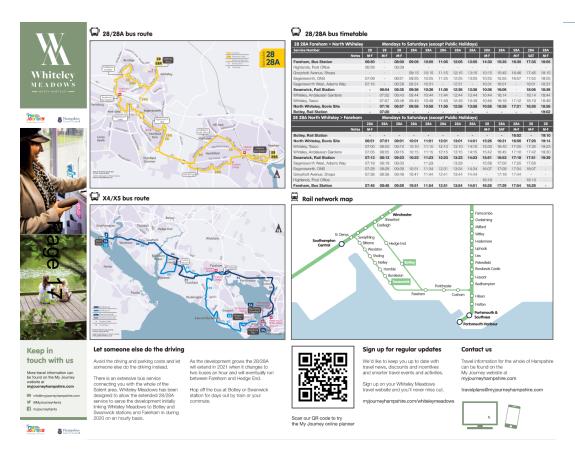

- Service 28/28 A started on 9th January 2023.
- Temporary Stops to start with
- Shelters to be installed later this year.





Issues – Errant Parking

- Temporary measures installed close to Cornerstone School. (Pictures Weds 12th July @ 09:30)
- Temporary Measures installed along Whiteley Way
- Consultation with HCC regarding introduction of further measures such as Double Yellow lines.
