
Public Document Pack Winchester City Council

Meeting North Whiteley Development Forum

Date and Time Monday, 15th July, 2024 at 6.00 pm.

7. Development update - verbal update - Jeff Davies











North Whiteley Development

Part of the Vistry Group

BRIEFING NOTE

North Whiteley Forum

Meeting 15th July 2024





Station Hil **Botley Road** Junction Northern Access Western Access Junction (WAJ) Curbridge Extension of Whiteley Way Extension of Bluebell Way Farm Roundabout Whiteley Town Centre Marjoram Way Parkway North Parkway South M27 Junction 9 A27 Proposed Highway Improvements Secondary School Primary School

North Whiteley Overview Plan November 2020 North Whiteley Consortium




Overview - Highways

- Development Highways & Whiteley Way R3 to R2 delivered by the North Whiteley Consortium
- M27 / R1 Parkway South Works Complete

North Whiteley Development – North Whiteley Forum BRIEFING NOTE - Meeting 15 July 2024



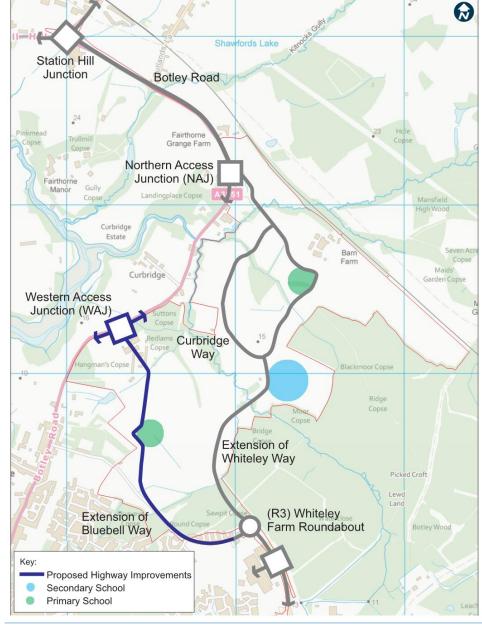

Phase 1 Bluebell Way Area

- Highway Opened to the Public 12th Feb 2021.
- Phase 1 Bus Service commenced 9th Jan 2023
- Further D. Yellow lines etc proposed
- Southern Local Centre:
 - Proposed Scheme under review
 - Contract drafted










Phase 1 Bluebell Way: (June 2024)



Phase 1 Bluebell Way South (July 2024)

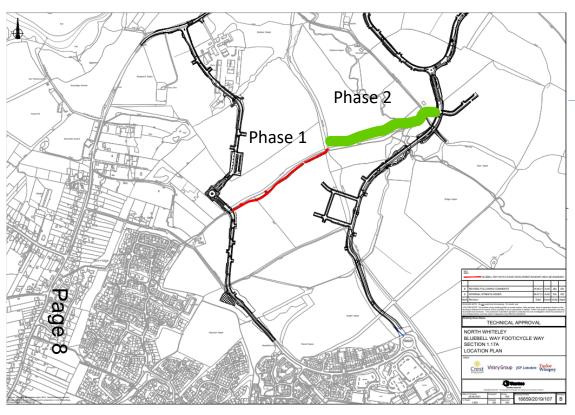


Strategic Cycleway: Footpath 9

- Phase 1 S278 Legal Agreement agreed in principle but still not completed:
 - Visibility Issues caused delays
 - Final Plans (almost) agreed with HCC.
 - Conclude s278 Agreement
 - Works can start once legal agreement in place.
- Phase 1 Footpath Diversion application approved (2023)
- Phase 1 Construction: Delayed again (Autumn 2024)
- Phase 2 Design underway Planning application
 Autumn 2024









0 Sawpit Watercl (R3) Whiteley .opse Farm Roundabout Copse Whiteley Town Centre Page (R2) Marjoram Way Whiteley (R1a) Parkway North Proposed Highway Improvements


Phase 2 - Off Site Whiteley Way

- Works commenced 11th March 2024
- Phase 1 Works underway
 - Significant culvert replacement works underway
 - Widening works R2- R3 (Tesco)
- Target Works Completion: Late 2025/ Early 2026

North Whiteley
Package 3 - NWC Whiteley Way
November 2020
North Whiteley Consortium





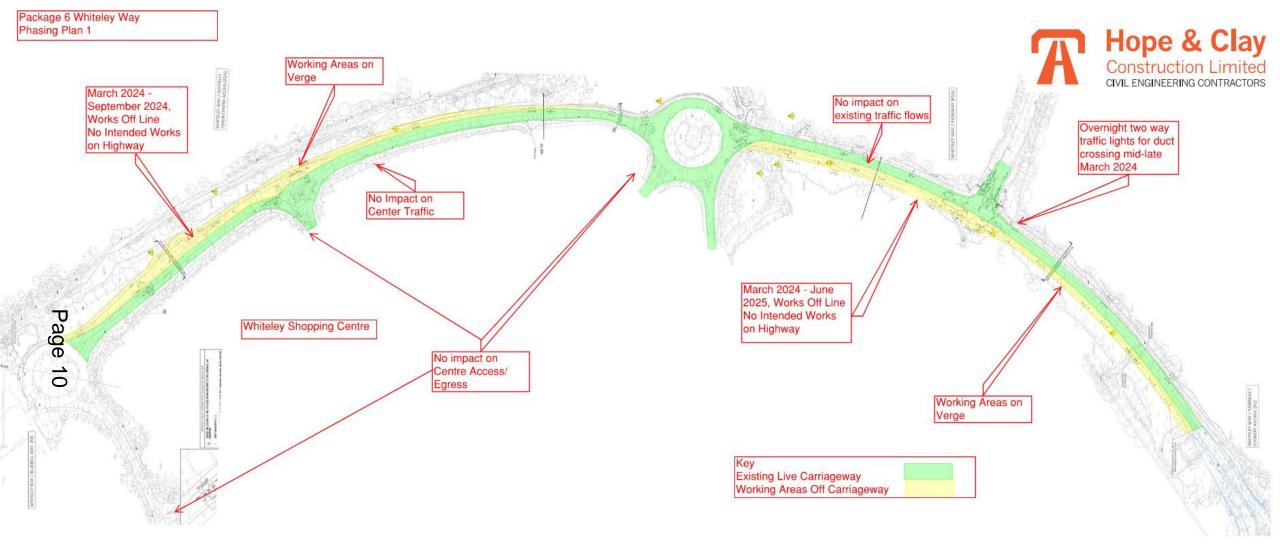

Whiteley Way Highway Improvements - Phase 1







(Shawfords Lake Station Hill Junction **Botley Road** Grange Farm Northern Access Junction (NAJ) Western Access Juncan (WAJ) Curbridge Way Extension of Whiteley Way (R3) Whiteley Extension of Farm Roundabout Botley Wood Bluebell Way Secondary School Primary School

Stantec

Phase 3 - Station Hill - Whiteley Way / **Curbridge Way to Whiteley Way**

- Whiteley & Curbridge Ways opened to through traffic 14 Sept 2023.
- Note that these roads run through Development areas under construction.
 - 20mph speed limit applied
 - Double Yellow Lines installed Sawpit Copse
 - Speed Humps (Sawpit Copse) installed.
- Secondary School: Anticipated start Spring 2025







Whiteley Way (North / East) (June 2024)



Whiteley/Curbridge Way - June 2024



Whiteley Gardens - June 2024

Housing Delivery (@ 17th June 2024)

Detailed Planning Permission granted for 3,172 Houses (89% of total)


2,034* Houses started

Of which 1,534* Houses Construction Mortgage Lending CML ready

Of which 1,519* Houses occupied


* Reporting incomplete



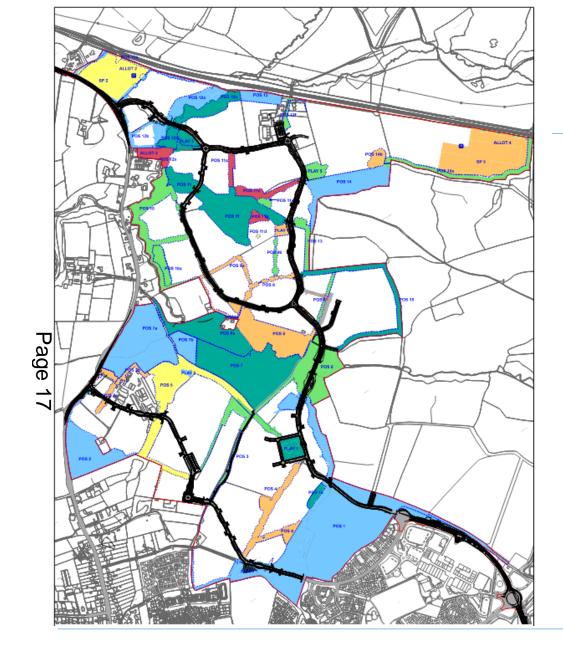

Open Space – Delivery Update

- Allotment 1 complete
- LEAP 2 (POS 5) & LEAP 3 (POS 12) completed
- LEAP 2 open. LEAP 1 Play Area open.
- Land Transfer Processes underway but still very slow.
- Landscape works underway
 - Area Group 1 POS 1, 2, 7A, 7B
 - Area Group 2 POS 1A, 7, 8A, 15
 - Highways (BB Way & Whiteley Way South)

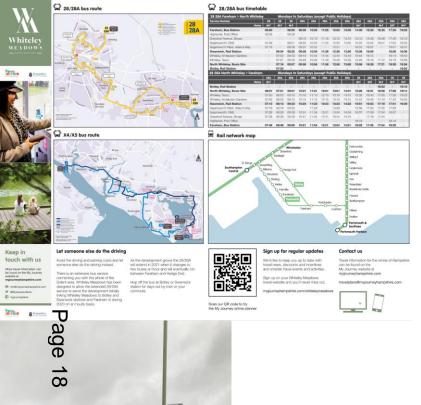

Bus Service

- Service 28/28 A reviewed.
 - New timetable from 1st July 2024
 - Optimised to focus on where the bus is being used
 - Amended to align with School journeys
- Potential Viability issue remains:
 - Demand slowly increasing
 - 4 year tender result disappointing
 - Review again in 2025

